



FAIRGROUNDS & PENNICHUCK MIDDLE SCHOOL ADDITIONS & RENOVATIONS

NASHUA, NEW HAMPSHIRE

JANUARY 2021 PROJECT UPDATES
HARVEY CONSTRUCTION





NASHUA
SCHOOL DISTRICT
Gateway to Opportunity



**PENNICHUCK MIDDLE
SCHOOL
CONSTRUCTION
PROGRESS MILESTONES**

SUBCONTRACTOR BIDDING IN PROGRESS
BID PACKAGE AWARDS (FEB 2021 – MAY 2021)



CONSTRUCTION START (SPRING 2021)

FAIRGROUNDS MIDDLE SCHOOL UPDATED HYBRID LEARNING & CONSTRUCTION LOGISTICS:

- INTENSIVE SPECIAL EDUCATION STUDENTS & STAFF RETURNED TO THE BUILDING ON TUESDAY, 1/19/2021
 - *BUILDING ACCESS/WAYFINDING WAS REVIEWED WITH SCHOOL ADMINISTRATION AND ESTABLISHED PRIOR TO STAFF/STUDENT RETURN*
- COORDINATING TURNOVER OF INTERIOR SPACES IN CONJUNCTION WITH SCHOOL ADMINISTRATION REQUIREMENTS & SCHOOL DISTRICT SCHEDULE
 - *CONSTRUCTION CLEANING/FINAL CLEANING BEING PERFORMED IN RENOVATED AREAS AND ADJACENT CLASSROOMS PRIOR TO OCCUPANCY*



TEMPORARY WALL CONSTRUCTION & BUILDING SAFETY MEASURES



- ALL ACTIVE CONSTRUCTION AREAS ARE SEPARATED BY TEMPORARY PARTITIONS (DRYWALL/POLY.)
 - LOCATED AT CENTRAL “OCTAGON” & ADMIN. AREAS
- NO UNACCOMPANIED WORKERS OUTSIDE OF CONSTRUCTION AREAS DURING SCHOOL HOURS

FAIRGROUNDS MIDDLE SCHOOL

UPCOMING CONSTRUCTION PROGRESS MILESTONES


INTERIOR RENOVATIONS & NEW ADDITION
(WINTER/SPRING 2021)



REMAINING SCIENCE ROOMS, GYMNASIUM,
& EXTERIOR SITE FURNISHING/CLEANUP
(SPRING/EARLY SUMMER 2021)

UPDATED FAIRGROUNDS CONSTRUCTION PHASING PLAN

- 6TH, 7TH, & 8TH GRADE STUDENT COMMONS AREAS (INCLUDING CORRIDORS)
 - READY FOR STUDENT/FACULTY OCCUPANCY UPON RETURN
- NEW ADMINISTRATION AREA & MAIN ENTRY ADDITION
 - MARCH 2021 COMPLETION
- ART, MUSIC, CTE, & MUSIC ROOMS
 - READY FOR STUDENT/FACULTY OCCUPANCY UPON RETURN
- SCIENCE PH. 1, ROBOTICS, ELL, & MATH/READING INTERVENTION ROOMS
 - APRIL 2021 COMPLETION
- SCIENCE PH. 2, GYMNASIUM, & EXTERIOR SITE FURNISHINGS/DEMobilIZATION
 - JUNE 2021 COMPLETION

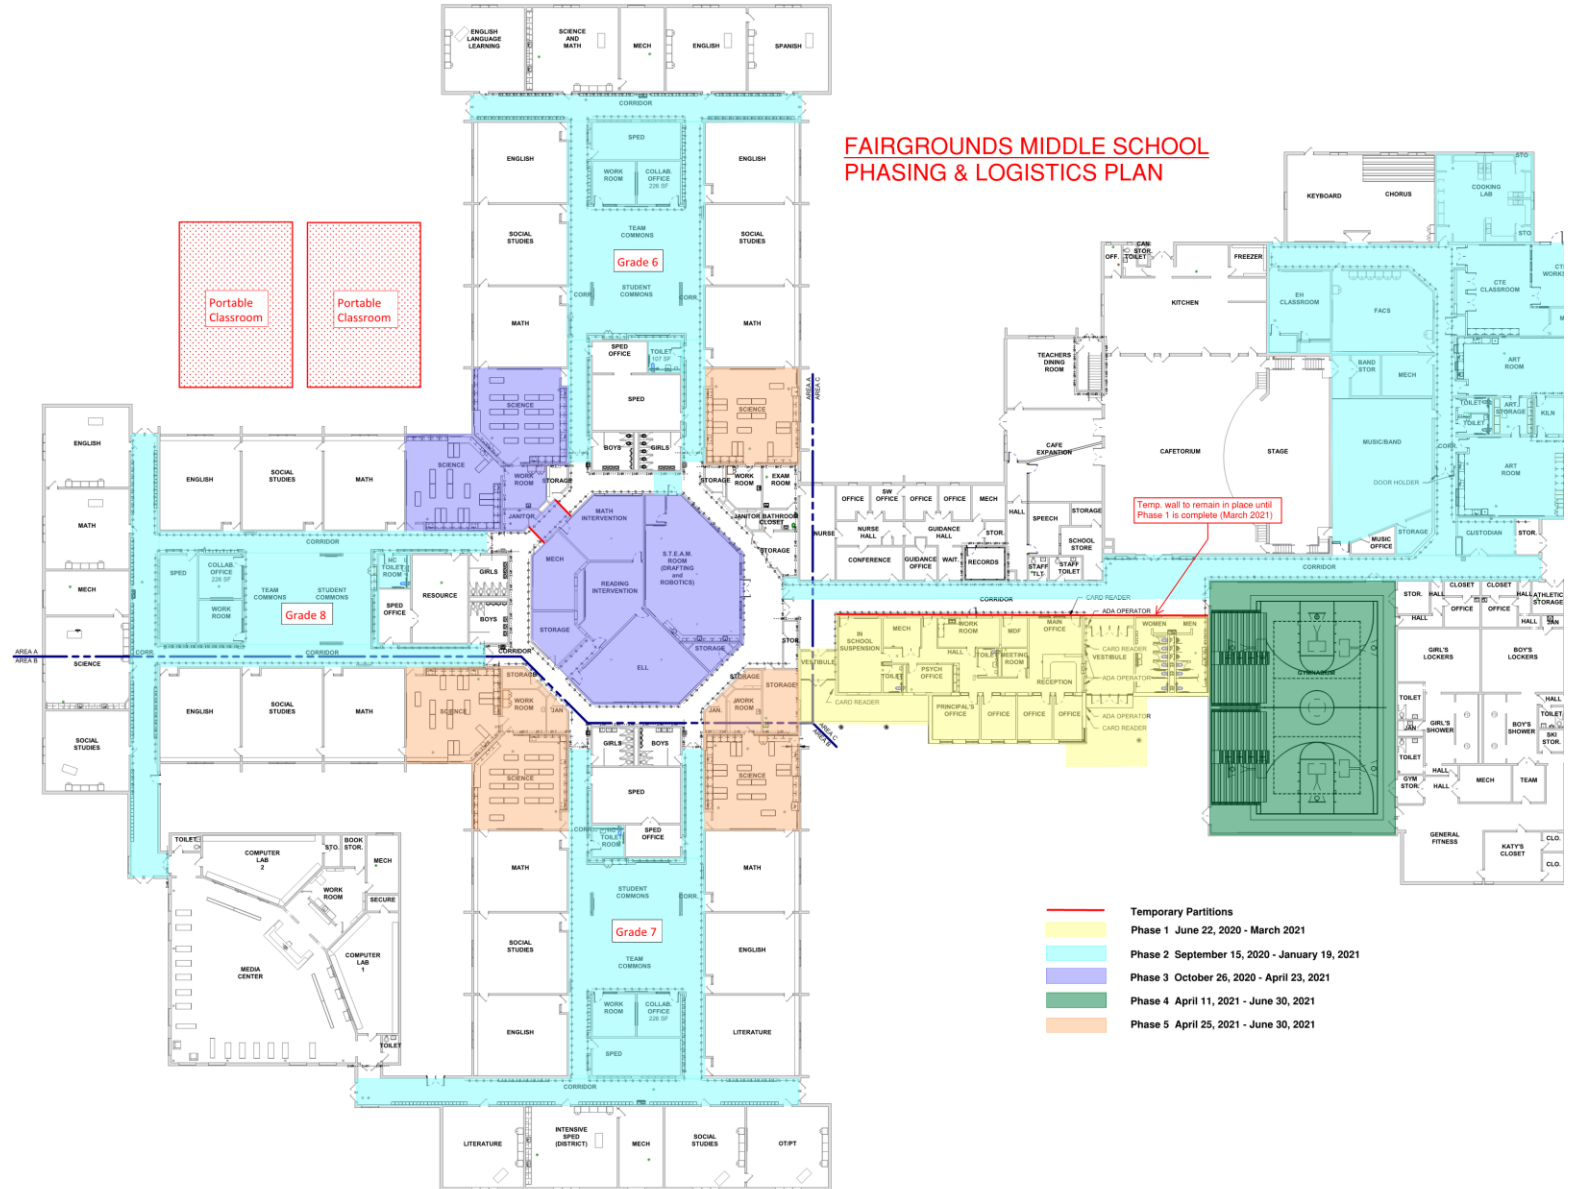

TEMPORARY PORTABLE CLASSROOMS

- 2 PORTABLE CLASSROOM STRUCTURES (4 TOTAL CLASSROOMS) LOCATED AT REAR OF SCHOOL
- OVERHEAD COVERAGE OF RAMPS AND LANDINGS FOR WEATHER PROTECTION
- SUBSTANTIALLY COMPLETE FOR TEACHER & STUDENT OCCUPANCY UPON RETURN





MAIN ENTRY & ADMINISTRATION RENOVATION

- WINTER CONSTRUCTION PROGRESS AT THE NEW MAIN ENTRY & CANOPY
- NEW SLAB AT INTERIOR





**TYPICAL COMPLETED
ADA-COMPLIANT
STAFF BATHROOM**



**STUDENT COMMONS RENOVATION
(TYPICAL FOR 6TH, 7TH, & 8TH
GRADE WINGS)**



MARKER BOARD
WRITING SURFACE



NEW DOUBLE-TIER
LOCKERS



STUDENT COMMONS RENOVATION (TYPICAL FOR 6TH, 7TH, & 8TH GRADE WINGS)



**TYPICAL WORK ROOM & COLLABORATION OFFICE
(6TH GRADE WING PICTURED)**



HARVEY
